

CMS Monthly Status Report -- HSU


March-2009

Student Admin 8.9 Implementation Status Detail

Implementation:	Student Admin 8.9
Live Production:	
GL #1-Adm & AA	10/08
GL #2-FA	03/09
GL #3-SR	04/09
GL #4-SFS	07/09
Project Status:	On Schedule
Impl'n Partner:	Oracle

Start Date	Milestone	Go-Live	End Date	Status
07/01/07	Academic Structure Defined	1	11/01/07	Complete
07/01/07	Course Catalog/Schedule Converted	1	01/28/08	Complete
07/01/07	Bio/Demo Data Loaded	1	11/01/07	Complete
07/01/07	Admissions Related Conversions Ready	1	02/01/08	Complete
12/15/07	SR Major Conversions MTP Ready	3	04/25/08	Complete
07/01/07	SR Configuration Complete	3	05/19/08	Complete
07/01/07	SR Business Processes Defined/Doc'd	3	02/13/09	Complete
07/01/07	SR Test Plans Created	3	02/15/09	Complete
07/01/07	SR Testing Complete	3	03/02/09	Complete
07/01/07	SR Mock MTP Complete	3	03/01/09	Complete
07/01/07	Build F09 Class Sched	3	03/17/09	Complete
07/01/07	FA Award Letters	2	03/27/09	Complete
08/01/08	SR Go Live	3	04/06/09	In-Progress
01/01/08	SF Go Live (Tuition Calc)	4	07/01/09	Not Started
08/01/08	Project Closure	n/a	10/01/09	

Planned vs Completed Tasks

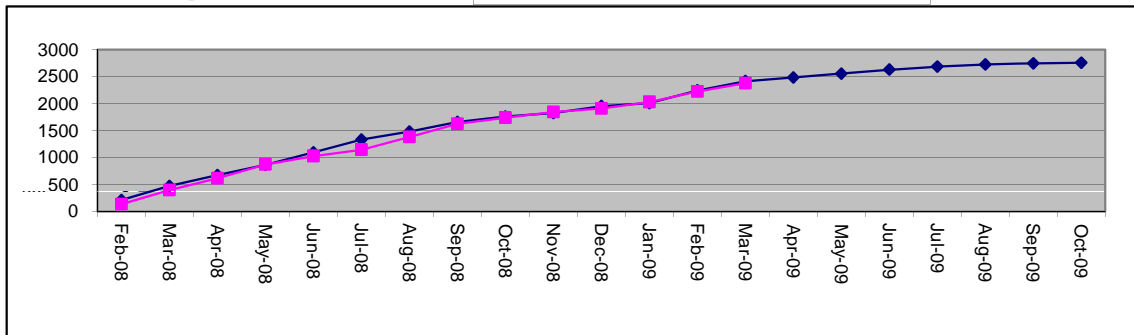

Recent Activity / Accomplishments (Last 30 Days):

- (1) Financial Aid live! Award letters sent to over 8,000 students on 03-19-09 and packaging completed for over 3,000 on 04-01.
- (2) DARS Advising live!
- (3) Faculty Center live!
- (4) Student Center usage continues to increase to positive feedback.
- (5) Student Records online schedule posted
- (6) Student Records enrollment appointments set & accessible in Student Center - on target for Registration go-live 04-06-09.
- (7) Resource 25 live!
- (8)
- (9)

Key Upcoming Activities (Next 30 Days):

- (1) Student Records Registration go-live 04-06-09
- (2)
- (3)
- (4)
- (5)
- (6)
- (7)

Current Issues / Concerns:

- (1) Will be monitoring performance closely with the 04-06-09 Registration go-live.
- (2)
- (3)
- (4)
- (5)
- (6)
- (7)
