



CMS Monthly Status Report -- HSU


June-2009

Student Admin 8.9 Implementation Status Detail

Implementation:	Student Admin 8.9
Live Production:	
GL #1-Adm & AA	10/08
GL #2-FA	03/09
GL #3-SR	04/09
GL #4-SFS	07/09
Project Status:	On Schedule
Impl'n Partner:	Oracle

Start Date	Milestone	Go-Live	End Date	Status
07/01/07	Academic Structure Defined	1	11/01/07	Complete
07/01/07	Course Catalog/Schedule Converted	1	01/28/08	Complete
07/01/07	Bio/Demo Data Loaded	1	11/01/07	Complete
07/01/07	Admissions Related Conversions Ready	1	02/01/08	Complete
12/15/07	SR Major Conversions MTP Ready	3	04/25/08	Complete
07/01/07	SR Configuration Complete	3	05/19/08	Complete
07/01/07	SR Business Processes Defined/Doc'd	3	02/13/09	Complete
07/01/07	SR Test Plans Created	3	02/15/09	Complete
07/01/07	SR Testing Complete	3	03/02/09	Complete
07/01/07	SR Mock MTP Complete	3	03/01/09	Complete
07/01/07	Build F09 Class Sched	3	03/17/09	Complete
07/01/07	FA Award Letters	2	03/27/09	Complete
08/01/08	SR Go Live	3	04/06/09	Complete
01/01/08	SF Go Live (Tuition Calc)	4	07/01/09	In progress
08/01/08	Project Closure	n/a	10/01/09	

Planned vs Completed Tasks

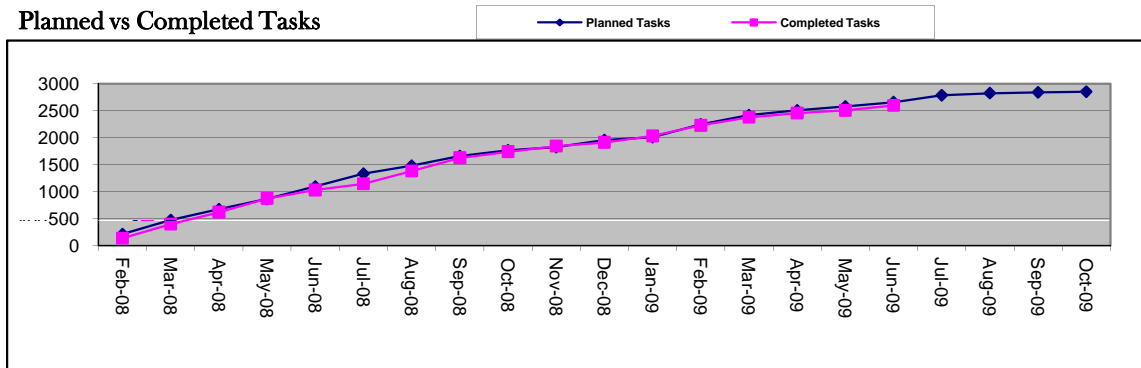

Recent Activity / Accomplishments (Last 30 Days):

- (1) Student Financials conversions complete. Ready for Production Tuition Calculation
- (2) Student Financials training completed.
- (3) Student Records HOP (Humboldt Orientation Program) registration successful for 2 sessions in June.
- (4) Financial Aid successfully tested Pell and loan origination. Ready for July.
- (6)
- (7)
- (8)
- (9)

Key Upcoming Activities (Next 30 Days):

- (1) Student Financials balance conversion and go-live
- (2) Financial Aid disbursements
- (3) Extended Education go-live
- (4)
- (5)
- (6)
- (7)

Current Issues / Concerns:

- (1)
- (2)
- (3)
- (4)
- (5)
- (6)
- (7)
