



# CMS Monthly Status Report -- HSU


## August-2009

### Student Admin 8.9 Implementation Status Detail

<b>Implementation:</b>	Student Admin 8.9
<b>Live Production:</b>	
<b>GL #1-Adm &amp; AA</b>	10/08
<b>GL #2-FA</b>	03/09
<b>GL #3-SR</b>	04/09
<b>GL #4-SFS</b>	07/09
<b>Project Status:</b>	On Schedule
<b>Impl'n Partner:</b>	Oracle

Start Date	Milestone	Go-Live	End Date	Status
07/01/07	Academic Structure Defined	1	11/01/07	Complete
07/01/07	Course Catalog/Schedule Converted	1	01/28/08	Complete
07/01/07	Bio/Demo Data Loaded	1	11/01/07	Complete
07/01/07	Admissions Related Conversions Ready	1	02/01/08	Complete
12/15/07	SR Major Conversions MTP Ready	3	04/25/08	Complete
07/01/07	SR Configuration Complete	3	05/19/08	Complete
07/01/07	SR Business Processes Defined/Doc'd	3	02/13/09	Complete
07/01/07	SR Test Plans Created	3	02/15/09	Complete
07/01/07	SR Testing Complete	3	03/02/09	Complete
07/01/07	SR Mock MTP Complete	3	03/01/09	Complete
07/01/07	Build F09 Class Sched	3	03/17/09	Complete
07/01/07	FA Award Letters	2	03/27/09	Complete
08/01/08	SR Go Live	3	04/06/09	Complete
01/01/08	SF Go Live (Tuition Calc)	4	07/01/09	Complete
08/01/08	Project Closure	n/a	10/01/09	

**Planned vs Completed Tasks**

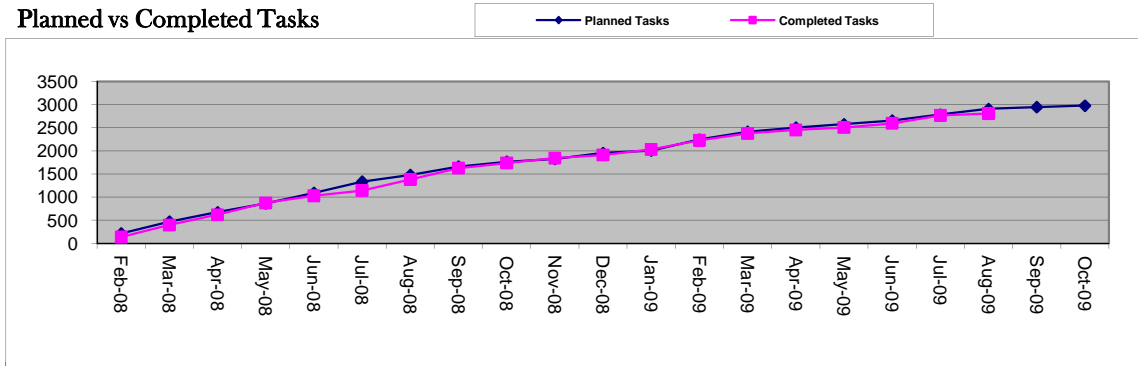

**Recent Activity / Accomplishments (Last 30 Days):**

- (1) Financial Aid disbursements processing successfully.
- (2) Housing Fee processing successfully.
- (3) First "peak period" for start of semester in PeopleSoft with minimal issues.
- (4) Immunization conversion completed from Banner to PeopleSoft
- (5)
- (6)
- (7)
- (8)

**Key Upcoming Activities (Next 30 Days):**

- (1) Honors and Awards Conversion
- (2)
- (3)
- (4)
- (5)
- (6)
- (7)

**Current Issues / Concerns:**

- (1)
- (2)
- (3)
- (4)
- (5)
- (6)
- (7)
